DIST	COUNTY	ROUTE	POST MILES TOTAL PROJECT	SHEET No	TOTAL SHEETS
04	Ala	80	2.0/2.3	71	83

REGISTERED STRUCTURAL ENGINEER — 06/26/2012 DATE

REGISTERED PROFESSIONAL ENGINEER — MEE SHING ONYANG — No. 2246 — STRUCTURAL — STATE OF CALIFORNIA

PLANS APPROVAL DATE

The State of California or its officers or agents shall not be responsible for the accuracy or completeness of electronic copies of this plan sheet.

Parsons Brinckerhoff
303 Second Street
Suite 700 North
San Francisco, CA 94107-1317

BAY AREA TOLL AUTHORITY
101 EIGHT STREET
OAKLAND, CA 94607

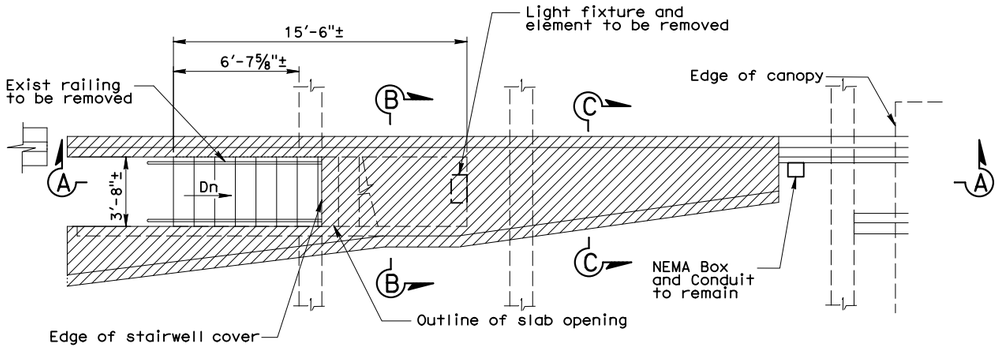

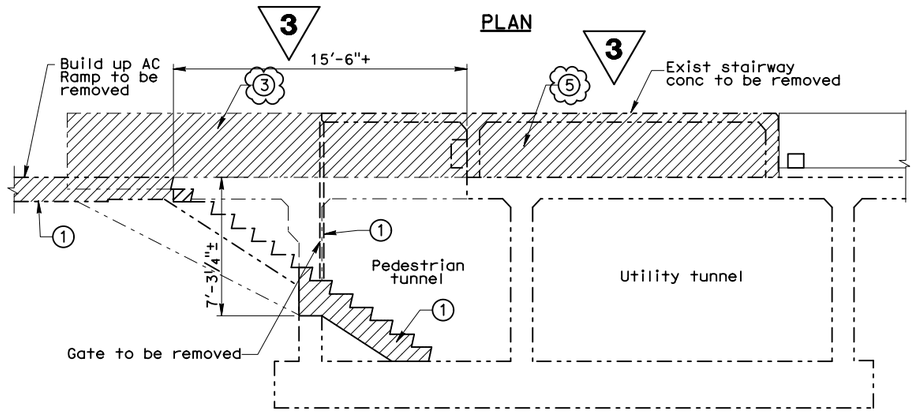

SECTION A-A

STAGE 1 - DEMOLITION

NO SCALE



SECTION B-B
NO SCALE

SECTION C-C
NO SCALE

LEGEND:

- To be removed
- Existing to remain
- ⊗ Construction staging

39' ≠ label as Addendum # 4

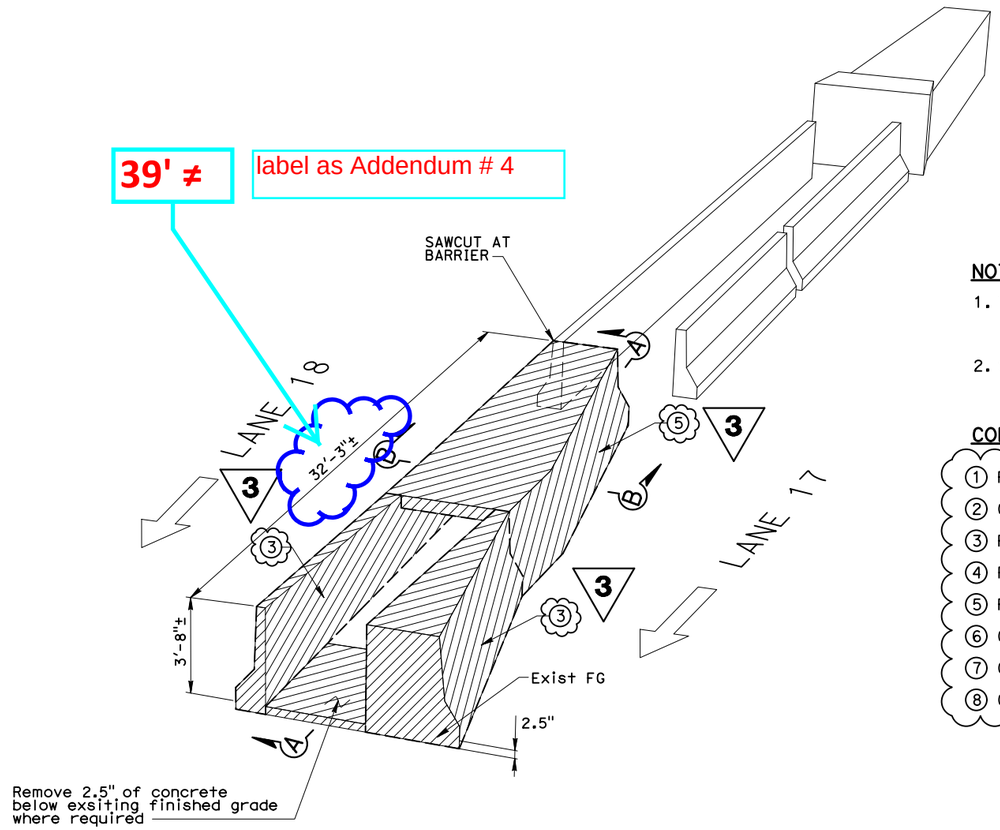

CRASH BARRIER

PERSPECTIVE VIEW
NO SCALE

NOTES:

1. The Contractor shall verify in the field all controlling dimensions before ordering or fabricating any materials.
2. See CALTRANS standard specifications for other specific requirements.

CONSTRUCTION STAGING

1. REMOVE STAIRS, GATE AND AC RAMP
2. CONSTRUCT WALL (SEE SHEET S-512)
3. REMOVE Conc. BARRIER
4. PLACE PCC BACKFILL (SEE SHEET S-512)
5. REMOVE Conc. LID
6. CONSTRUCT PCC SLAB (SEE SHEET S-512)
7. CONSTRUCT PAVEMENT
8. CONSTRUCT ANCHORED K-RAIL

3

3 **Revised Per Addendum No. 4 dated August 24, 2012**

2012

AS-511

DESIGN	BY	CHECKED	PREPARED FOR THE STATE OF CALIFORNIA DEPARTMENT OF TRANSPORTATION	PROJECT ENGINEER	BRIDGE NO.	SFOBB TOLL PLAZA CANOPY RENOVATIONS
DETAILS	BY	CHECKED			POST MILE	STAIRWAY NO.7 REMOVAL
QUANTITIES	BY	CHECKED				

DESIGN DETAIL SHEET (ENGLISH) (REV. 2/25/05)

ORIGINAL SCALE IN INCHES FOR REDUCED PLANS 0 1 2 3

CU BATA011
EA 4G2801/4G2901

DISREGARD PRINTS BEARING EARLIER REVISION DATES →

REVISION DATES (PRELIMINARY STAGE ONLY)

SHEET 52 OF 64

FILE => AS-511.dgn

USERNAME => ReyesL DATE PLOTTED => 15-AUG-2012 TIME PLOTTED => 10:17
